


WIS 23 North and Galena Street Project

- 10 additional culvert pipe replacements (locations shown on the map and also attached) – tentative schedule:
 - Thursday 7/14: pipe #9, then pipe #8
 - Friday 7/15: likely pipes #7 & #6
 - Monday 7/18: likely pipes #5 & #4
 - Pipes #1, #2, #3, and #10 TBD, but likely the week of 7/25
- Bridge work:
 - 7/14: final concrete pour for bridge parapets
 - Next week: bridge crew to remove falsework & forms, demobilize equipment
 - Week of 7/25: grading for bridge approaches, slopes, and riprap
 - Week of 8/1: concrete approach slabs, asphalt for roadway tie-ins
 - Week of 8/7: the goal is to open the bridge up to LOCAL TRAFFIC ONLY
- Slope grading along guardrail areas throughout project limits to continue next few weeks
- Asphalt paving is likely to start the week of August 7th and continue through the end of August
- The following work will continue for the next few weeks:
 - Water main and storm sewer pipe installations from Huntington Court to Center Hill Road

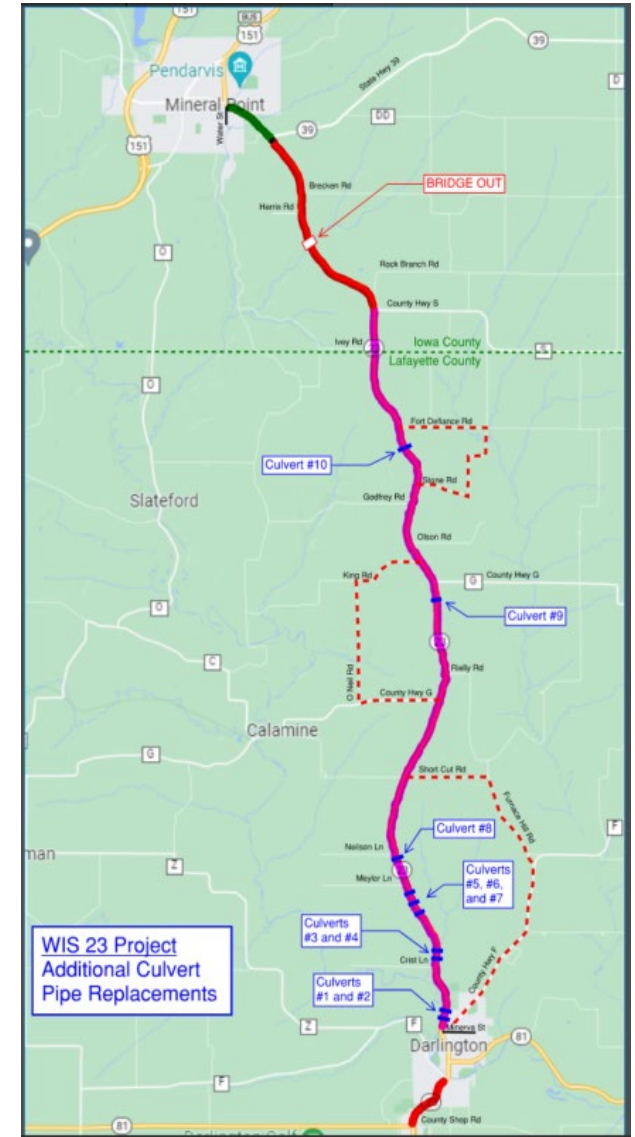

- Roadway grading from Hill Street to the south
- Block retaining wall construction
- On Tuesday 7/19 and Wednesday 7/20:
 - Crew scheduled to be on-site to apply polymer overlay to bridge deck
 - The overlay will be completed half at a time under lane closure with flagging operations – expect delays
