


WIS 23 project from Darlington to Mineral Point:

- Bridge work is complete, but road closed barricades will remain in place on each side until all paving and guardrail work is finished.
 - Entire roadway remains closed to through traffic; open only to local traffic and emergency vehicles.
- Milling and asphalt paving started this week and will continue into early/mid-September.
 - Crew started at Crist Lane and should be paved up to Nielson Lane by the end of this week.
 - Plan is to continue north up to Mineral Point (Water St), then drop back and pave the section from Darlington (Minerva St) to Crist Lane.
- September into October: gravel shouldering, new guardrail installation, rumble strips, pavement markings.
- Early October still anticipated for completion.



Huntington Court scheduled to be paved next Thursday, August 24th

- Block retaining wall construction along the west side of Galena St from S. Huntington Court up to Union Grove Lane scheduled to resume the week of Labor Day.
- Below is what the final roadway section will look like, it's starting to come together with the walls, curb and sidewalk.

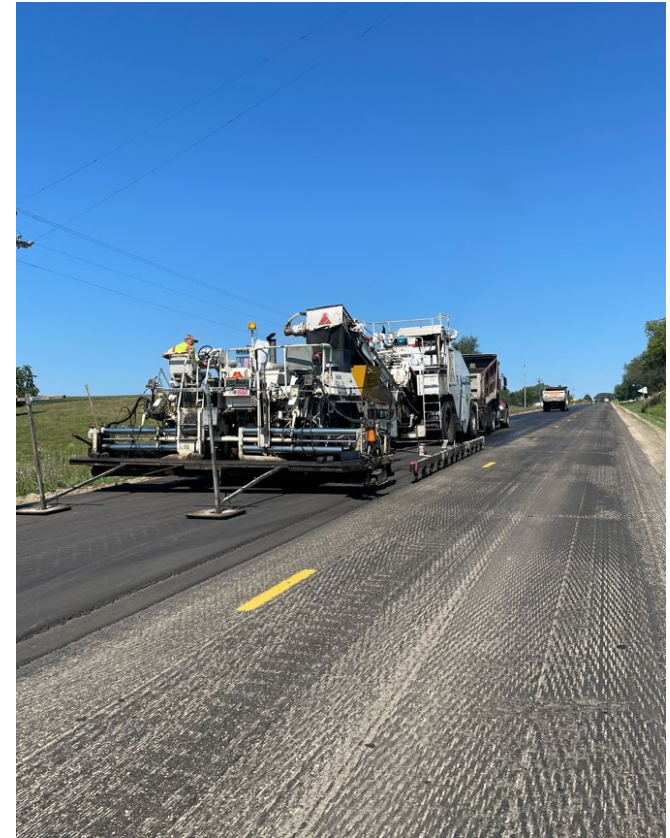

WIS 23/Galena Street project in Darlington:

- Water main and sanitary sewer pipe work completed.
- Storm sewer pipe work will continue next 2 weeks up to Center Hill Road, hoping to be complete by Labor Day weekend.
- Roadway grading and rock placement will continue next several weeks, working their way up the hill from S. Huntington Court.
- Lower layer of asphalt pavement from Ravine St to S.
